

Exam Questions PK0-004

CompTIA Project+ Certification Exam

<https://www.2passeasy.com/dumps/PK0-004/>



NEW QUESTION 1

A project manager is releasing resources and archiving documents. Which of the following phases is the project MOST likely in?

- A. Initiation
- B. Planning
- C. Monitor and control
- D. Closing

Answer: D

NEW QUESTION 2

Which of the following are characteristics of a project? (Choose two.)

- A. Ongoing
- B. Temporary
- C. Start and finish
- D. Achieving a goal
- E. Consisting of milestones
- F. Restricting the budget

Answer: BC

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 27

NEW QUESTION 3

Which of the following roles has approval authority for project funding?

- A. Champion
- B. Chief Financial Officer (CFO)
- C. Project Management Office (PMO)
- D. Sponsor

Answer: D

Explanation:

References <https://books.google.com.pk/books?id=scjmDQAAQBAJ&pg=PA29&lpg=PA29&dq=comptia+roles+has+appr>

NEW QUESTION 4

A project is coming to the end of a phase. The PMO required that the quality team review the work and budget before moving on to the next phase of the project. The project manager must schedule the review of the phase and have the stakeholders present. This review is referred to as:

- A. change management.
- B. a milestone.
- C. a tollgate.
- D. an incident response.

Answer: B

NEW QUESTION 5

An outsourced project team member approaches the project manager and complains that the contract does not permit overtime. The project manager had fast-tracked tasks that require additional hours. Which of the following documents did the project manager fail to reference?

- A. MOU
- B. MOA
- C. SOW
- D. SLA

Answer: B

NEW QUESTION 6

Which of the following is a schedule that illustrates the duration of an activity?

- A. Process diagram
- B. Ishikawa Diagram
- C. Gantt chart
- D. Pareto chart

Answer: C

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 168

NEW QUESTION 7

A milestone task on the critical path has been completed. Which of the following should the project manager notify?

- A. Owner of predecessor task
- B. Project team
- C. Project sponsor
- D. Project steering committee

Answer: C

NEW QUESTION 8

Several team members report that meeting objectives are not being met.

Which of the following documents would a project manager create to make team meetings more effective? (Choose two.)

- A. Create an SOW prior to each meeting and adhere to it.
- B. Create a meeting agenda prior to each meeting and adhere to it.
- C. Create a lessons learned list prior to each meeting and adhere to it.
- D. Create a project charter prior to each meeting and adhere to it.
- E. Create an action item list during the meeting and adhere to it.
- F. Create a corrective action plan prior to each meeting and adhere to it.
- G. Create a WBS prior to each meeting and adhere to it.

Answer: BE

NEW QUESTION 9

When forming a project team, there are a number of phases.

When a project team is productive and effective this phase is known as which of the following?

- A. Forming
- B. Norming
- C. Performing
- D. Storming

Answer: C

NEW QUESTION 10

A project manager has contracted a third-party vendor to achieve milestones. Which of the following risk strategies is the project manager applying?

- A. Transfer
- B. Accept
- C. Avoid
- D. Mitigate

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 238

NEW QUESTION 10

ABusiness has implemented a new online performance management tool that allows functional and project managers to rate employees online.

This action is known as which of the following?

- A. Business process change
- B. Organizational change
- C. Internal reorganization
- D. Business continuity planning

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 297

NEW QUESTION 14

A project manager is justifying a required change with the associated impact on the project. Which of the following is the NEXT step?

- A. Implementation
- B. Approval
- C. Validation
- D. Auditing

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 294

NEW QUESTION 17

An industry leader may be joining the project team and can potentially provide additional expertise. Which of the following strategies should the project manager

employ?

- A. Exploitation
- B. Acceptance
- C. Validation
- D. Transfer

Answer: C

NEW QUESTION 18

Three IT companies have agreed to summarize their efforts as a common organization to generate new businesses in the IT cloud computing industry. Which of the following is the type of organizational change described?

- A. Expansion
- B. Rightsizing
- C. Merger
- D. Onboarding

Answer: C

NEW QUESTION 20

During a project, a key stakeholder asks a project team member to add a requirement. The team member adds the requirement without informing the project manager. Which of the following is described in this scenario?

- A. Change request
- B. Risk mitigation
- C. Change control
- D. Scope creep

Answer: D

NEW QUESTION 21

An agreement document that is intended to prevent two or more organizations from sharing specific, confidential information with anyone but each other is called:

- A. an RFP.
- B. an NDA.
- C. an SLA.
- D. an MOU.

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 302

NEW QUESTION 26

A project team completed ABrainstorming activity to determine potential issues with a project. Which of the following activities should the project team do NEXT?

- A. Risk identification
- B. Risk quantification
- C. Risk planning
- D. Risk response

Answer: A

NEW QUESTION 31

Which of the following statements are correct regarding project management? (Select two.)

- A. A project can be part of an organization's program management.
- B. An organization's portfolio will include programs.
- C. A program has ADefined start and finish.
- D. An organization's portfolio is a temporary and unique endeavor.
- E. A project portfolio will be managed under program management.

Answer: BC

NEW QUESTION 34

A team has been assembled and assigned a project to reduce recent, unanticipated production cost overruns. Which of the following tools should the project team select to determine the possible origins of the increased costs?

- A. Pareto chart
- B. Fishbone diagram
- C. Process diagram
- D. Run chart

Answer: B

NEW QUESTION 37

Which of the following techniques modifies the schedule based upon resource constraints?

- A. Critical Chain Method
- B. Critical Path Method
- C. Arrow Diagramming Method
- D. Precedence Diagramming Method

Answer: A

NEW QUESTION 42

A company hires an outside vendor to provide 24/7 support.

Which of the following documents would determine the contractual obligations?

- A. PO
- B. SLA
- C. LOI
- D. MOU

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 303

NEW QUESTION 45

Which of the following Agile ceremonies is used to determine the backlog items that will be worked on the next weeks?

- A. SCRUM retrospective meeting
- B. Sprint planning meeting
- C. Daily standup meeting
- D. Review meeting

Answer: B

Explanation:

References: <https://www.atlassian.com/agile/ceremonies>

NEW QUESTION 47

A project team is comprised of a mix of in-house and virtual team members.

When a complex announcement needs to go out to the entire project team, which of the following is the MOST effective way to communicate it?

- A. Composing a project team email with the details of the announcement is the best method.
- B. It gives the project manager the opportunity to explain but not be overcome with questions from the team.
- C. Using text messaging to make the announcement is the best method.
- D. It allows the project manager to reach the project team members wherever they are located.
- E. Sending a fax is the best method.
- F. It gives the project manager the opportunity to explain the announcement and come up with questions and answers the team may have.
- G. Hosting a webConference meeting is the best method.
- H. It gives the project manager the opportunity to explain the announcement and answer any questions from the team.

Answer: D

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 260

NEW QUESTION 51

While working on risk ranking, the project team is unsure about the qualitative scales to be used for probability and impact. The project manager directs the team to look in the:

- A. quality plan.
- B. project management plan.
- C. risk register.
- D. process diagram.

Answer: A

NEW QUESTION 52

A non-stakeholder approaches the project manager and asks if certain items can be added to a project that was started two months earlier. Which of the following constraints does this impact MOST?

- A. Time
- B. Schedule
- C. Scope
- D. Cost

Answer: D

NEW QUESTION 56

A project manager must create documentation before the project kickoff meeting. Which of the following documents will identify the project, introduce the project manager, and establish authority in the project?

- A. Responsibility matrix
- B. Resource allocation plan
- C. Project charter
- D. Statement of work

Answer: C

NEW QUESTION 58

A project manager is creating the monthly report for top management. The project manager has collected the information below:

AC = 100

PV = 80

EV = 120

Based on this information, the CPI reflects which of the following about the project?

- A. It is under budget.
- B. It is over budget.
- C. It is ahead of schedule.
- D. It is behind schedule.

Answer: A

Explanation:

“The cost performance index (CPI) is calculated this way: $CPI = EV / AC$ ”

Excerpt From: Kim Heldman. “CompTIA Project+ Study Guide.” iBooks.

NEW QUESTION 61

A project manager is assigned to an ongoing project. Which of the following is the FIRST document the project manager should review?

- A. Project schedule
- B. Action items
- C. Project charter
- D. Communication plan

Answer: A

NEW QUESTION 66

In which of the following situations is a project manager MOST likely to use a process diagram?

- A. When describing a new business idea for the team to review
- B. When describing a new business workflow for the team to implement
- C. When describing a new business project for the team to implement
- D. When describing a new business acquisition for the team to review

Answer: B

NEW QUESTION 70

The PM is preparing for the planning phase kickoff meeting. It is imperative for the team to focus during the meeting on the expected outcomes.

Which of the following best describes what the PM should work on FIRST?

- A. Project charter
- B. Project schedule
- C. Meeting agenda
- D. Responsibility assignment matrix
- E. Risk register

Answer: B

NEW QUESTION 75

A governance committee has just approved a new project. The project scheduler is now developing the project schedule. Which of the following activities should be done FIRST?

- A. Add durations.
- B. Add the start and finish dates
- C. Add tasks.
- D. Add resources.

Answer: C

NEW QUESTION 77

The client accepts the critical design review.

Which of the following meetings should be held to move to the NEXT step in the project?

- A. Execution
- B. Kickoff
- C. Closure
- D. Planning

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 112

NEW QUESTION 80

A company is in the process of combining the human resources and marketing departments. Which of the following describes this change?

- A. Business process change
- B. Business merger
- C. Internal reorganization
- D. Interorganizational change

Answer: A

NEW QUESTION 85

A project manager is trying to explain to a stakeholder why projects are progressively elaborated upon. Which of the following is the BEST Explanation:?

- A. In the beginning, projects entail A Degree of uncertainty that needs to be specified.
- B. In the beginning, projects have start and finish dates that require elaboration.
- C. In the beginning, projects are part of a program that requires coordination.
- D. In the beginning, projects start with detailed inputs that need to be explained.

Answer: A

NEW QUESTION 90

A project manager has noticed poor attendance at status meetings.

Which of the following strategies should the project manager use to improve attendance? (Choose two.)

- A. Provide an agenda Before the status meeting.
- B. Adhere to an agenda and scheduled time.
- C. Add non-project-related items to the agenda.
- D. Add and discuss new agenda items throughout the meeting.
- E. Discard the action items at the conclusion of the meeting.

Answer: AB

NEW QUESTION 94

A new project charter is being drafted.

Which of the following would be the BEST source for the high-level project requirements?

- A. Sponsor
- B. Project manager
- C. Project management office
- D. Project team

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 108

NEW QUESTION 95

Which of the following activity sequencing techniques uses nodes to symbolize the dependencies of each activity?

- A. Critical Path Method
- B. Critical Chain Method
- C. Arrow Diagramming Method
- D. Gantt Chart Method

Answer: C

NEW QUESTION 97

A part that is needed to complete Task 3 has been backordered and will arrive three days later than scheduled. Task 3 must be complete for Task 4 to start. There is one day of float for the two tasks. Which of the following represents the number of days the project schedule will be delayed?

- A. Zero
- B. One
- C. Two
- D. Three

Answer: D

NEW QUESTION 100

Which of the following defines the minimum level of engagement of a stakeholder?

- A. Passive
- B. Invested
- C. Contributing
- D. Interested

Answer: A

NEW QUESTION 102

A project manager is assigned to a project and has not had a handover meeting with the previous project manager. The new project manager is reviewing the percent of project completion, schedule progress, and budget constraints.

Which of the following documents should the project manager use to obtain this information?

- A. Project schedule
- B. Balanced scorecard
- C. Issue log
- D. Status report

Answer: D

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 328

NEW QUESTION 105

A critical stakeholder has requested additional status updated beyond the schedule.

Which of the following factors MOST likely needs to be accounted for when communicating with this stakeholder?

- A. Confidentiality
- B. Criticality
- C. Frequency
- D. Cultural differences

Answer: C

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 265

NEW QUESTION 110

A project team has finished creating a WBS and started developing a schedule. The team should FIRST determine the:

- A. durations.
- B. tasks.
- C. critical path.
- D. resources.

Answer: B

NEW QUESTION 115

A customer has requested additional features for an active project. Which of the following steps should take place NEXT?

- A. Implement the requested changes.
- B. Evaluate the impact of the changes.
- C. Update all project documents.
- D. Submit the requested changes to the CCB.

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 293

NEW QUESTION 120

A project's key stakeholders have requested significant changes that will affect the scope. To adjust the project scope, which of the following need to be changed? (Choose two.)

- A. Cost performance parameter
- B. Project schedule
- C. KPI
- D. Corrective action plan
- E. WBS

Answer: BE

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 133

<https://books.google.co.za/books?id=evR0gPFBHJ4C&pg=PA128&lpg=PA128&dq=complete+a+project+soon>

NEW QUESTION 124

Which of the following describes how a project is related to a program?

- A. A program is a combination of multiple projects.
- B. A program contains an element of the project.
- C. A program is a part of a project.
- D. A program uses half of the project's budget.

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 72

NEW QUESTION 129

The project schedule performance index is 1.1, and the cost performance index is 0.9. Which of the following describes the project status?

- A. Ahead of schedule and over budget
- B. Behind schedule and under budget
- C. Ahead of schedule and under budget
- D. Behind schedule and over budget

Answer: C

NEW QUESTION 134

Which of the following activities are associated with the closing phase of a project? (Choose two.)

- A. Risk mitigation
- B. Archiving of project documents
- C. Tracking of expenditures
- D. Lessons learned
- E. Quality assurance

Answer: BD

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 338, 339

NEW QUESTION 135

In a project with a of \$235,000, the CPI is 0.80, and the SPI is 1.20. Based on this information, which of the following can the key stakeholders determine about the project?

- A. The project is under budget and ahead of schedule.
- B. The project is over budget and ahead of schedule.
- C. The project is under budget and behind schedule.
- D. The project is over budget and behind schedule.

Answer: A

NEW QUESTION 136

Which of the following project documents should be used to record the occurrence of an unplanned event?

- A. Action log
- B. Risk log
- C. Change log
- D. Issue log

Answer: D

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 327

NEW QUESTION 137

Which of the following risk strategies prevents a risk from impacting a project?

- A. Accept risk
- B. Mitigate risk
- C. Avoid risk
- D. Transfer risk

Answer: C

Explanation:

Reference <https://pm4id.org/chapter/11-2-risk-management-process/>

NEW QUESTION 140

A vendor was removed from a company due to non-performance but continues to submit invoices for work that was not completed. Which of the following should the project manager do to stop the vendor from sending invoices?

- A. Draft a C&D letter and send it to vendor.
- B. Review the MOU with the vendor.
- C. Ask the legal departments to draft a non-complete agreement for the vendor to sign.
- D. Meet with the finance department to prevent the vendor from sending invoices.

Answer: A

NEW QUESTION 145

A vendor is unable to deliver an order by the specified date.

Which of the following should be the project manager's NEXT steps? (Choose two.)

- A. The project manager should notify the affected project team and, if necessary, adjust the schedule because the project could potentially encounter delays.
- B. The project manager should notify the project sponsor to update the schedule in the documentation because the project could potentially encounter delays.
- C. The project manager should adjust the schedule in the documentation and, if necessary, take steps to rush other areas of the schedule so the project will not encounter delays.
- D. The project manager should update the project management plan in the documentation to reflect the reason for the possible delay in the project timeline.
- E. The project manager should update the procurement plan and action items to reflect the possible delay in the project timeline.

Answer: AD

NEW QUESTION 150

A customer has stated that meeting the project schedule and milestones takes priority and is, therefore, willing to spend additional funds to sustain operations. The project team must ensure completion of the:

- A. business continuity plan.
- B. incident response plan.
- C. disaster recovery plan.
- D. risk management plan.
- E. quality management plan.

Answer: D

NEW QUESTION 154

During the execution phase, the project manager discovered that the testing phase is dependent on completion of the vendor's tasks. The project team has just informed the project manager their activities are almost complete, and they would like permission to begin testing. The vendor is not scheduled to deliver the products for two months.

Which of the following should have occurred to prevent this issue?

- A. During the planning phase, the project manager should have recognized the relationship between the vendor's and project team's tasks and adjusted the schedule for the project team to begin activities two months later.
- B. The project manager should have crashed the schedule for the vendor to keep it at the same work pace as the rest of the project team.
- C. During the project team's regular status meeting with the vendor, the project team should have informed the vendor that the team was ahead of schedule and to speed up their work.
- D. During the project team's regular status meeting with the vendor, the vendor should have informed the project team that it required another two months, and to slow down.

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 170

NEW QUESTION 157

Which of the following is ADefinition of an RFP?

- A. ADocument sent to potential vendors to solicit ABid for a project.
- B. ADocument sent to potential vendors to request information for skills and experience for a project.
- C. ADocument sent to potential vendors to request a commitment for a project.
- D. ADocument sent to potential vendors to solicit information that excludes pricing information for a project.

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 300

NEW QUESTION 161

A team member learns that an assigned task is not due until the very end of the project. Moreover, the team member is not aware of any predecessor tasks dependent on completing the assigned task. Which of the following does the project manager use to decide if the team member can start the task later or earlier?

- A. Review the PERT chart and evaluate if the task is a critical dependency.
- B. Review the PERT chart and evaluate if the task is ADiscretionary dependency.
- C. Review the PERT chart and evaluate if the task is a real dependency.
- D. Review the PERT chart and evaluate if the task is an external dependency.

Answer:

B

Explanation:

References

<http://www.pmgloss.com/comptia/>

NEW QUESTION 163

A key stakeholder asks the project manager for additional features. Which of the following documents should the project manager refer to before responding to this request?

- A. Process diagram
- B. Change control plan
- C. Balanced scorecard
- D. SWOT matrix

Answer: B

NEW QUESTION 164

A customer asks a project manager if a small change can be made during the delivery phase. The project manager does not agree to the change. Which of the following is the MOST likely reason?

- A. Established communication plan
- B. Scope creep
- C. Resource constraints
- D. Iterative approach

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 133

NEW QUESTION 168

A customer will have ongoing changes to project requirements. Which of the following is the BEST project management methodology for this requirement?

- A. Waterfall
- B. Agile
- C. PRINCE2
- D. Bottom-up

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 310

NEW QUESTION 172

A project manager needs to track the actual and estimated start and finish dates of all WBS work packages. Which of the following is a necessary step to record the actual durations?

- A. Establish each WBS work package resource.
- B. Establish and set the baseline.
- C. Establish and set the quality gates.
- D. Establish the tollgates.

Answer: B

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 167

NEW QUESTION 174

Which of the following measurements would give the project manager the BEST estimate of the total cost of an active project?

- A. EAC
- B. BAC
- C. TCPI
- D. ETC

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 232

NEW QUESTION 175

The project's network map has a loop with multiple project outcomes. This is the result of which of the following scheduling tools?

- A. Establishing project schedule baselines

- B. Critical Path Analysis
- C. Critical Chain Method
- D. Graphical evaluation and review technique

Answer: D

NEW QUESTION 177

A project team added a new member who has proprietary information about a competitor's product. The team member was suddenly removed from the project. Which of the following MOST likely occurred?

- A. The company received a C&D.
- B. A higher-priority project needed the expertise.
- C. The new member did not sign an NDA.
- D. An SLA prevented new team members.

Answer: A

NEW QUESTION 180

A project team is spread between two countries on different continents. Which of the following factors are MOST likely to influence communication methods selected for the communication plan? (Select TWO).

- A. Interorganizational constraints
- B. Personal preferences
- C. Language barriers
- D. Cultural differences
- E. Confidentiality constraints

Answer: CD

NEW QUESTION 185

A subcontractor has submitted design documentation on the deliverable due date, but it will require rework. The activity is on the critical path of the project schedule. Which of the following should the project manager do NEXT?

- A. Determine the expected duration of the rework and complete a change request to modify the project baselines.
- B. Notify the project sponsor to schedule and facilitate a team meeting to rework the design documentation.
- C. Determine the expected duration of the rework with any associated quality control activities and add the duration to an updated version of the WBS.
- D. Update the master project schedule, and distribute it all stakeholders in accordance with the project communications plan.

Answer: A

NEW QUESTION 189

The final project report should contain which of the following?

- A. Minutes of all the project meetings
- B. Project design documentation
- C. Detailed breakdown of the schedule
- D. Summary of the project cost

Answer: D

NEW QUESTION 193

A program manager informs a project manager that a new, high-priority project has been approved and will need the current project's resources before the scheduled project close date. The project team meets and determines that the project should be fast-tracked.

Which of the following documents should the project team reference to fast-track the project? (Choose two.)

- A. Scope management plan
- B. Configuration management plan
- C. Network diagram
- D. Project schedule
- E. Project plan

Answer: CD

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 171

NEW QUESTION 196

A project manager noticed the development team supporting a project does not have sufficient skills to complete the development phase. The project manager has discussed this issue with the functional manager and agreed to continue with the development phase due to time restrictions. Which of the following strategies is the project manager applying?

- A. Accepting
- B. Mitigating
- C. Avoiding
- D. Transferring

Answer:


A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 238

NEW QUESTION 199

During the execution phase of a project, a project task has run longer than anticipated.

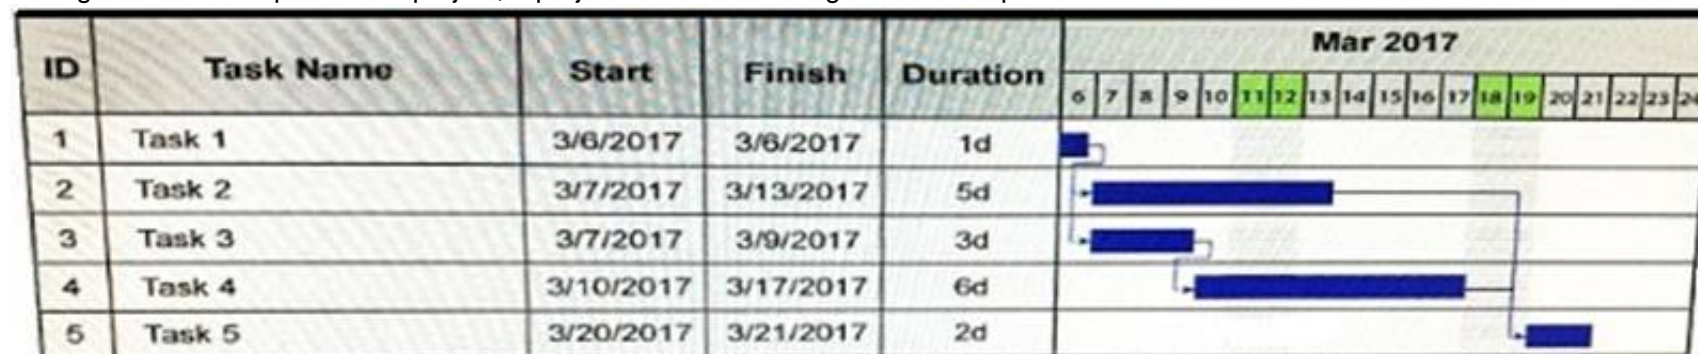

Which of the following is the new critical path of the project if Task 2 requires an additional two days to complete?

- A. 12 days
- B. 14 days
- C. 16 days
- D. 19 days

Answer: A

Explanation:

References: Kim Heldman, CompTIA Project+ Study Guide, 2nd Edition, Sybex, Indianapolis, 2017, p. 169

NEW QUESTION 201

A project manager is managing a transactional project. One of the key team members is having difficulties understanding the client requirements. Which of the following actions would be BEST for the project manager to take?

- A. Ask the client to provide additional language resources to the team.
- B. Purchase a language translation program.
- C. Hire a translator to help the key team member
- D. Ask the client to provide requirements in the native language of the team.

Answer: D

NEW QUESTION 202

The design activity of a project has the following cost attributes: PV = 100,000

EV = 20,000

AC = 90,000

Based on this scenario, calculate the schedule variance.

- A. -80,000
- B. -70,000
- C. 10,000
- D. 120,000

Answer: A

NEW QUESTION 205

A project manager receives a call from the area regional building department and is informed that, upon inspection, waterlines from public water access to the project building do not meet local material and installation code specifications. Which of the following items BEST describes the unmet objective?

- A. Schedule
- B. Milestone
- C. Gate
- D. Task

Answer: D

NEW QUESTION 206

.....

THANKS FOR TRYING THE DEMO OF OUR PRODUCT

Visit Our Site to Purchase the Full Set of Actual PK0-004 Exam Questions With Answers.

We Also Provide Practice Exam Software That Simulates Real Exam Environment And Has Many Self-Assessment Features. Order the PK0-004 Product From:

<https://www.2passeasy.com/dumps/PK0-004/>

Money Back Guarantee

PK0-004 Practice Exam Features:

- * PK0-004 Questions and Answers Updated Frequently
- * PK0-004 Practice Questions Verified by Expert Senior Certified Staff
- * PK0-004 Most Realistic Questions that Guarantee you a Pass on Your FirstTry
- * PK0-004 Practice Test Questions in Multiple Choice Formats and Updatesfor 1 Year
